

Pending Civil & Electromechanical works at 50LL and 7LL WDS in Puzhal zone along with HSC, Interconnection works and construction of Sluice and Air Valve Chambers

Preamble:


- This scheme provides comprehensive water supply to Puzhal, Puthagaram, Surapet and Kathirvedu which are the added area to the GCC. Scheme consists of completing pending Civil works and Electromechanical works at 50LL and 7LL OHTs of in Puzhal and KS Nagar respectively.
- 2) The estimate amount for the work is Rs.729.2 Lakhs under JNNURM & CMCDM funds of 2017-18 vide G.O Ms.No.105, MA&WS (MW) Dept. Dt: 11.07.2013.

Scope:

Scheme consists of completing pending Civil works and Electromechanical works at 50LL and 7LL OHTs of in Puzhal and KS Nagar respectively along with construction of Sluice and Air valve chambers

Contractor:

The work was awarded to M/s.N R & Co in joint venture with M/s. Sri Rajeswari Constructions on 10.09.2019 with a contract period of 12 months.

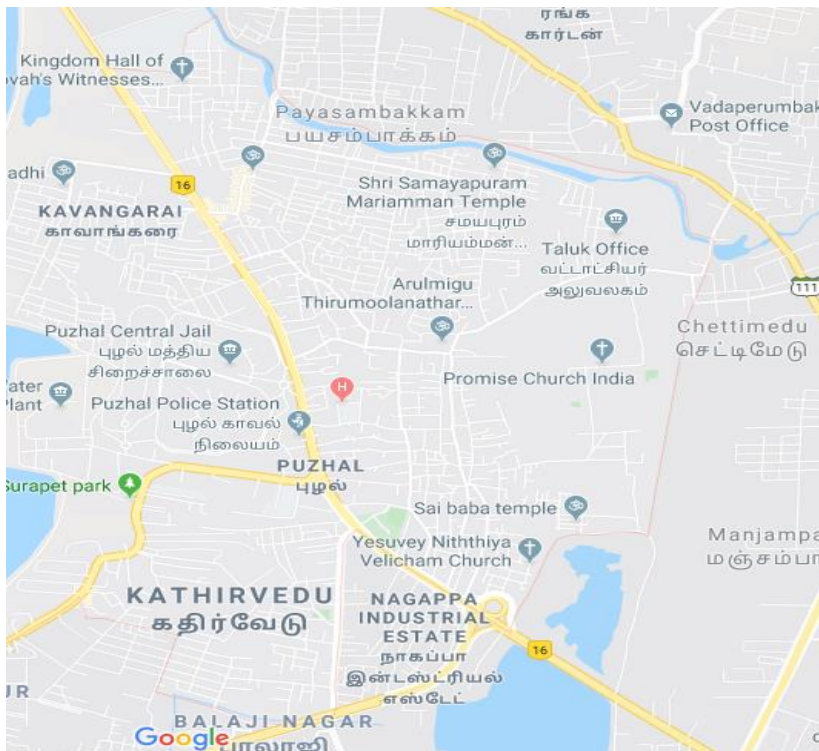

Progress & Status of the work:

- The work has been commenced and 1151 nos of HSC given. Fourteen percent of Civil and Electromechanical works done. 32.5% of Work completed.
- Probable Date of Completion 31.03.2021.
