


PERUNGUDIWSS

- Perungudi is one among the 42 local bodies added in the expanded Chennai city. Perungudi has an extent of 4.64 square Km. falls in Divisions 186 &184 Area XIV of Expanded Corporation of Chennai it consists of 305 streets. The total length of the road/streets for Perungudi is 45.845 Km.

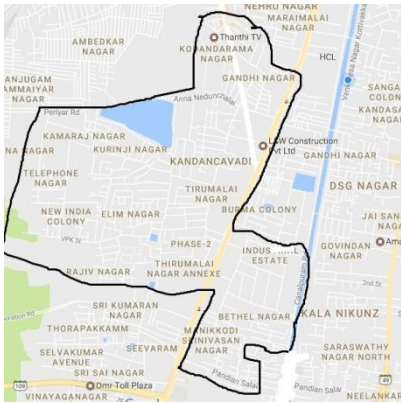

- The population to be benefited by implementation of Scheme are 49860, 88113 and 155714 in the year 2014, year 2029 and year 2044 respectively at the rate of water demand 7.70 MLD, 13.70 MLD and 24.20 MLD for the above corresponding years.
- The scheme cost for “Providing Comprehensive Water supply scheme to Perungudi” is Rs.4100 lakhs. The Government in its GO (MS) no 105 MAWS (MC.I) Department Dated 11.07.2013 has issued orders for the implementation of Chennai Mega City Development Mission. Technical sanctioned was awarded on 11.07.2013 for Rs.4100 lakhs.
- **The Components of work**
 1. Laying of DI Distribution mains of sizes ranging from 100mm to 1000mm dia for a length of 48545 m.
 2. Laying of conveying mains of 500 mm DI pipes for a length of 1200 m.
 3. Construction of UGT 6.00 LL and OHT 45.00 LL and pump house at Veerapandiayan Kattabomman Street , Perungudi.
 4. Providing House Service Connections of 7200nos.

➤ **Contract details**

The work was awarded to M/s Abhiram Infra Projects Pvt. Ltd. on 04.03.2014 for a contract value of Rs. 2587.15 lakhs. The works commenced on 28.05.2014. The contract period is 24 months. Scheduled date of completion was 27.05.2016.

➤ **Progress of work (as on 14.02.2020) :**

- | | |
|--------------------------------|--------------|
| 1. Physical progress | - 96%. |
| 2. Financial progress | - 78.28%. |
| 3. Probable date of completion | - 30-06-2020 |
